



TOWN OF DISCOVERY BAY SKATEPARK #6176

DISCOVERY BAY, CA




20 YEAR WARRANTY

FASTENER FREE RIDING SURFACE



MAXGRIP™ POLYESTER POWDERCOAT 3/16" STEEL RIDING SURFACE

WWW.AMERICANRAMPCOMPANY.COM

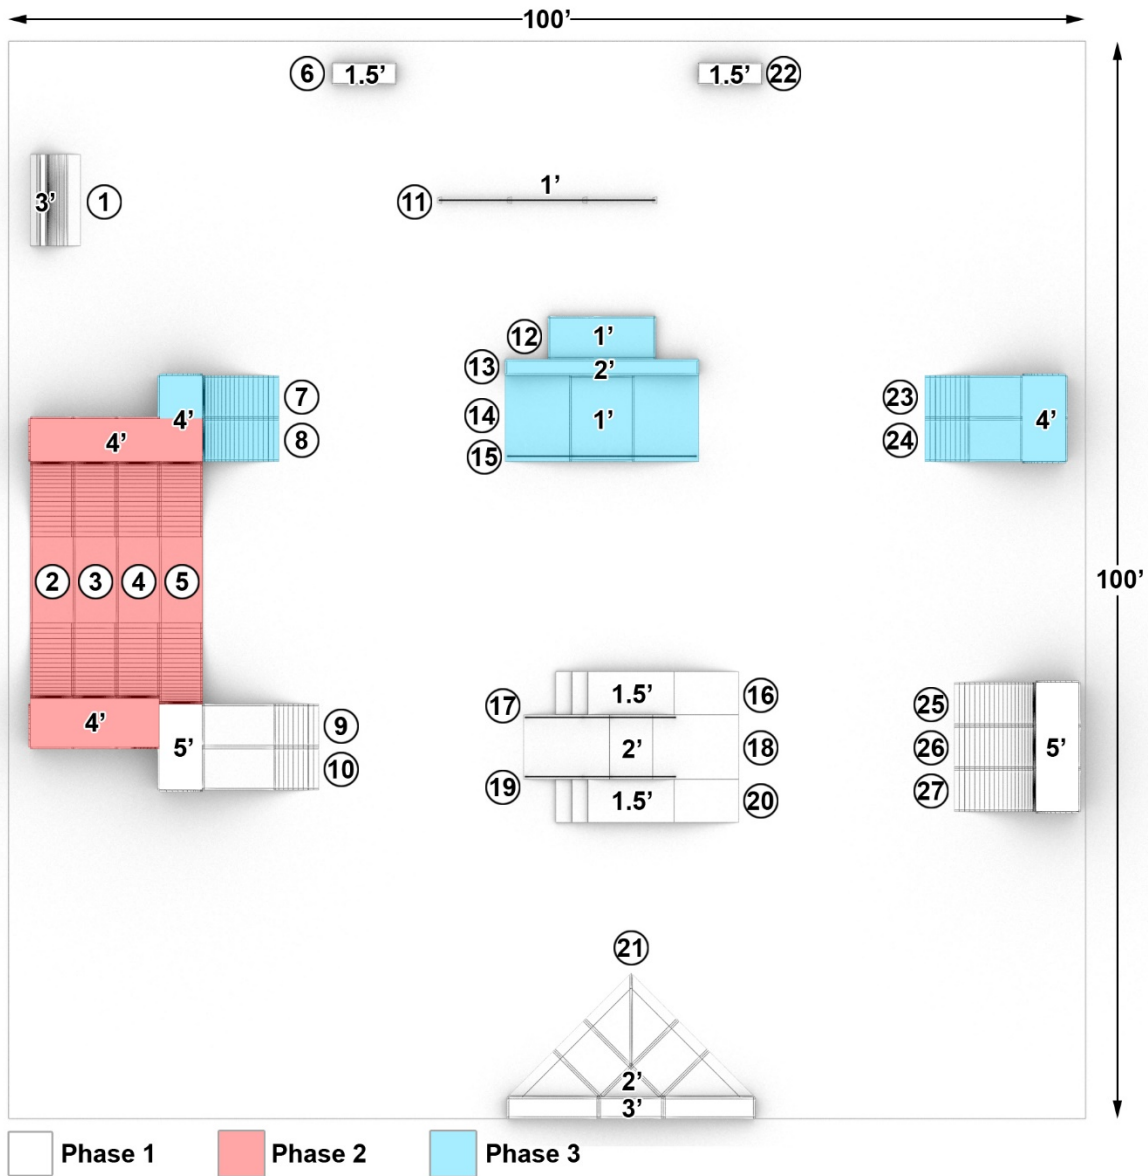

[CLICK HERE TO VIEW DESIGN RENDERINGS](#)



601 McKinley
Joplin, MO 64801
Tel: (417) 206-6816
Toll Free: (800) 949-2024
Fax: (417) 206-6888

sales@americanrampcompany.com

DRAWN BY Chuck Dodge

DATE 4/11/16

REP. AGENCY


American Ramp Company

REP. NAME

Alex Alekhine

REP. PHONE

(417) 206-6816



CUSTOMER APPROVAL **DATE**

PARK ENCLOSED? Yes

PRO SERIES ✓

X SERIES -

STEALTH SERIES -

STEALTH CLASSIC SERIES -

PROJECT NAME

**Town of Discovery Bay
Skate Park**

DESIGN NO. 6176

601 McKinley
 Joplin, MO 64801
 Toll-free 877-RAMP-778
 Local 417-206-6816
 Fax 417-206-6888
sales@americanrampcompany.com



Quote #	Design #	FOB
03798_CD	6176	Discovery Bay, CA

Phase 1

<u>Ite</u> <u>m</u>	<u>Obstacle</u>	<u>Height</u>	<u>Width</u>	<u>Length</u>
1	Jersey Barrier (Replica Series)	3.0'	8.5'	4.5'
6	Skate Bench (Concrete)	1.5'	2.0'	6.0'
9	Bank Ramp	5.0'	4.0'	15.0'
10	Bank Ramp	5.0'	4.0'	15.0'
11	Grind Rail (Round)	1.0'	2"	20.0'
16	Wedge, Flat, Stair	1.5'	4.0'	17.0'
17	Grind Rail, Kinked (Round)	1.5'	2"	14.0'
18	Wedge, Flat, Wedge	2.0'	6.0'	20.0'
19	Grind Rail, Kinked (Round)	1.5'	2"	14.0'
20	Wedge, Flat, Stair	1.5'	4.0'	17.0'
21	Pyramid, Hipped w/3' Ledge	3.0'	13.5'	24.0'
22	Skate Bench (Concrete)	1.5'	2.0'	6.0'
25	Quarter Pipe	5.0'	4.0'	12.0'
26	Quarter Pipe	5.0'	4.0'	12.0'
27	Quarter Pipe	5.0'	4.0'	12.0'

Subtotal	\$56,857.31
Framework Enclosures	\$5,685.73
Freight	FREE
Supervised Installation	\$4,373.64
8.5% Sales Tax	\$5,687.92

TOTAL **\$72,604.60**

Estimated Monthly Payment, 5 Year Term \$1,459.35

Phase 2

<u>Ite</u> <u>m</u>	<u>Obstacle</u>	<u>Height</u>	<u>Width</u>	<u>Length</u>
2	Half Pipe	4.0'	4.0'	30.5'
3	Half Pipe	4.0'	4.0'	30.5'
4	Half Pipe	4.0'	4.0'	30.5'
5	Half Pipe	5.0'	4.0'	26.5'

Subtotal	\$31,636.16
Framework Enclosures	\$3,163.62

Freight	FREE
Supervised Installation	\$2,433.55
8.5% Sales Tax	\$3,164.83

TOTAL	\$40,398.17
--------------	--------------------

Estimated Monthly Payment, 5 Year Term	\$812.00
--	----------

Phase 3

<u>Item</u>	<u>Obstacle</u>	<u>Height</u>	<u>Width</u>	<u>Length</u>
7	Quarter Pipe	4.0'	4.0'	11.0'
8	Quarter Pipe	4.0'	4.0'	7.0'
12	Grindbox	1.0'	4.0'	10.0'
13	Hubba Ledge (Replica Series)	2.0'	1.5'	18.0'
14	Wedge, Flat, Wedge	1.0'	8.0'	18.0'
15	Grind Rail (Round)	1.0'	2"	18.0'
23	Bank Ramp	4.0'	4.0'	13.0'
24	Bank Ramp	4.0'	4.0'	13.0'

Subtotal	\$29,675.37
Framework Enclosures	\$2,967.54
Freight	FREE
Supervised Installation	\$2,282.72
8.5% Sales Tax	\$2,968.68

TOTAL	\$37,894.30
--------------	--------------------

Estimated Monthly Payment, 5 Year Term	\$761.68
--	----------

Signature:

Date:

Notes:

- Framework Enclosures Optional.
- Prevailing wage included. For full install, double the supervised installation cost.
- Estimated Monthly Payment is based on a Tax-Exempt Municipal Lease. Final rates are subject to credit review and/or market changes in the index rate. For more options/information please contact our Finance Partner:
 - Chris Canavati with NCL at 866-763-7600 or chris@lscfinancial.com
- If your project is subject to bonding requirements, call for revised quote.



Purchase through our competitively bid government NJPA contract.
WE LOOK FORWARD TO BUILDING YOU A GREAT SKATE PARK!
